



ePortal Update 2011 Statistics

- 35,000 Documents filed
- 6,155 Registered users
- 1,517 Users that have filed



ePortal Update 2011 Statistics


Monthly Percentage Increase in Filings

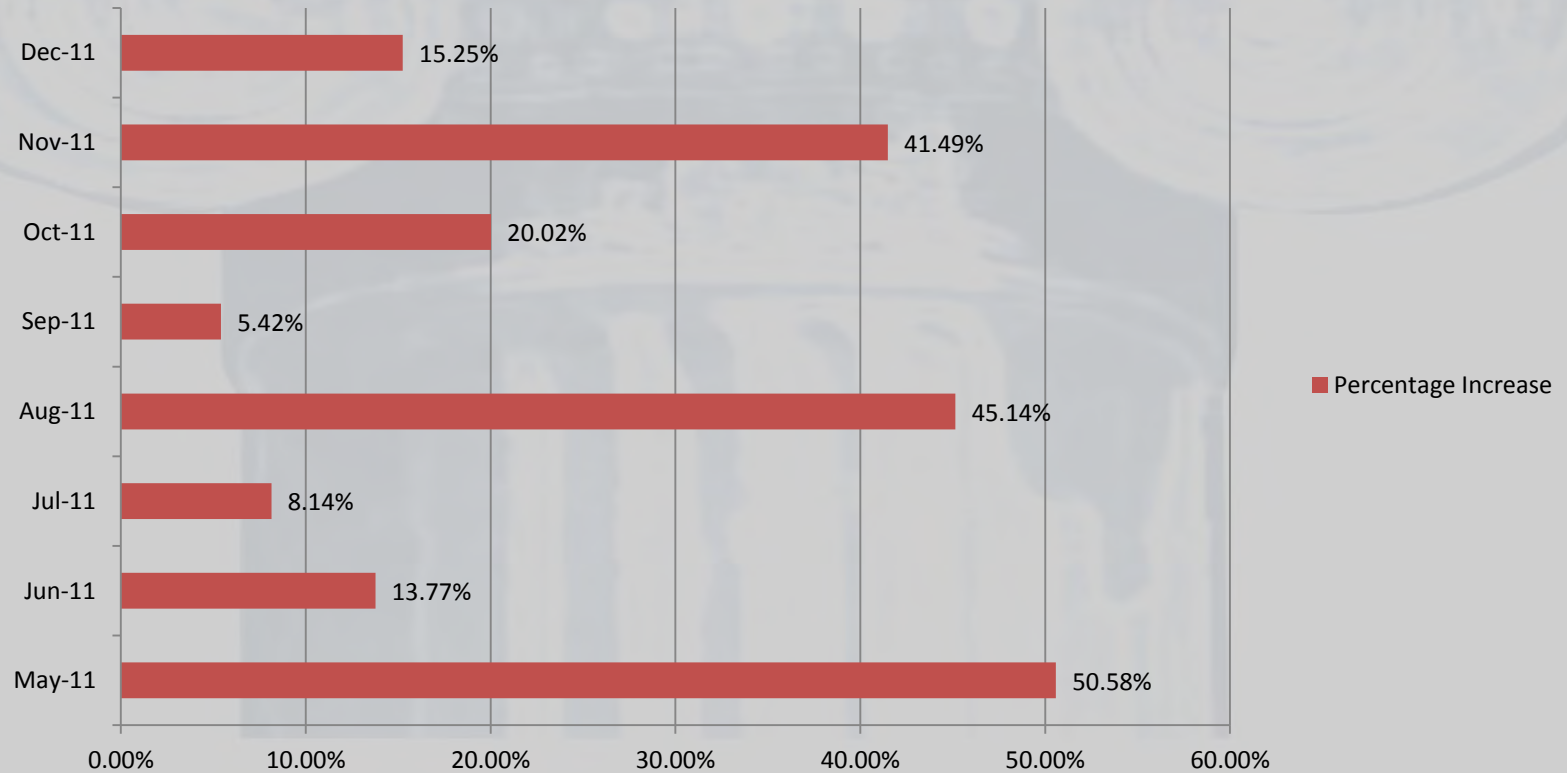



ePortal Development Priorities For 2012


- Quarterly releases
(Deficiencies/Enhancements)
- Criminal e-filing functionality
- Appellate/Supreme Court
functionality
- Mandated changes
- eService



ePortal Development Status

- Quarterly releases
 - 4th Quarter 2011 Release complete - 1/23/2012
 - Addressed 50 Deficiencies/20 Enhancements (Full list posted on website)
 - Ability for Clerks to collect additional fees associated with filings including Summons, Additional Parties and Lis Pendens fees
 - Enhanced Reporting Capability
 - Enhancements and increased validations for Credit Card Processing
 - ePortal Review and Code Maintenance Enhancements
 - Presented at 1/24/2012 Statewide WebEx

[@myflcourtagency.com](http://myflcourtagency.com)




ePortal Development Status

- Criminal e-filing functionality
 - Portal staff working with State Attorney Association Technical Group
 - Conference calls held on 11/17/11, 12/1/11, 1/27/12
 - Initial Design Document under review



ePortal Development Priorities For 2012


- Appellate/Supreme Court functionality
 - Weekly design meetings ongoing
 - Requirements/Design Documents
 - Phase 1 complete, development in progress
 - Phase 2 in progress



ePortal Implementation Status

- Counties with capability to accept filings through the ePortal (41)


Alachua	Gilchrist	Leon	Suwannee
Baker	Glades	Liberty	Union
Bay	Gulf	Madison	Wakulla
Bradford	Hamilton	Marion	Walton
Broward	Hardee	Martin	Washington
Calhoun	Hendry	Miami-Dade	
Charlotte	Holmes	Okeechobee	
Collier	Jackson	Palm Beach	
Columbia	Jefferson	Polk	
Dixie	Lafayette	Putnam	
Duval	Lake	Santa Rosa	
Franklin	Lee	St. Lucie	



ePortal Implementation Status (Continued)

- Counties linked to ePortal (5)


Clay
Manatee
Orange
Pasco
Sarasota



ePortal Implementation Status (Continued)

- Counties in process (21)
- FACC project manager has begun working with each county to develop an implementation plan to meet the 2012 deadlines

Brevard
Citrus
Desoto
Escambia
Flagler
Gadsden
Hernando
Highlands
Hillsborough
Indian River
Levy
Monroe
Nassau
Okaloosa
Osceola
Pinellas
Seminole
St. Johns
Sumter
Taylor
Volusia




Florida Courts E-Filing Authority

ePortal Implementation Status

Wednesday, February 1, 2012


21 "In-Process" Counties



21 “In-Process” Counties

Strategic Business Goal:


Ensure that all counties have the capability to accept electronic filings for Civil Court cases by July 1, 2012, via the E-Filing Court Records Portal (ePortal)



21 “In-Process” Counties

Tactical Business Objectives:


1. Load each county’s E-Filing Codes into the ePortal
2. Verify each county’s access to an electronic queue enabling review, approval, and transmittal of E-Filings into their local CMS
3. Demonstrate each county’s capability for comprehensive, “end-to-end” processing of E-Filed Civil cases



21 “In-Process” Counties

Assumptions & Constraints:


- Each county will determine whether to implement E-Filing for the 5 Civil Divisions all at once or in a phased approach
- Usage of the ePortal and meeting the July 1 deadline **does not** mean that E-Filing is mandatory or that all filings are handled by the ePortal
- It **does mean** that the capability exists, has been verified, and is available



21 “In-Process” Counties

County Dashboard


- FACC staff conducted conference calls with the counties in December to assess readiness, challenges, and to offer assistance
- This was followed by an email in mid-January requesting additional implementation information
- The county-by-county “dashboard” status report that follows is the result of these information gathering activities



21 "In-Process" Counties

County Dashboard


County	Status	Target Date Provided
Brevard	Meeting with their vendor on 2/1; working on Implementation Plan details	N/A
Citrus	Working through Implementation Plan	06/15/2012
Desoto	Clericus Implementation Plan (FACC)	04/27/2012
Escambia	Addressing CMS integration issues	Early April
Flagler	Implementation Plan in place for phased implementation	03/12/2012
Gadsden	E-Filing Codes setup in-process	N/A



21 “In-Process” Counties

County Dashboard


County	Status	Target Date Provided
Hernando	Clericus Implementation Plan (FACC)	03/09/2012
Highlands	Clericus Implementation Plan (FACC)	04/06/2012
Hillsborough	4 Divisions going live with Portal by target date; Juvenile tied to new CMS migration & scheduled to be live on Portal by 4th Quarter 2012/1st Quarter 2013	2013
Indian River	Working through Implementation Plan	02/20/2012
Levy	Working on developing an Implementation Plan	June 2012
Monroe	Working through Implementation Plan; 1 Division currently scheduled to be ready by target date; other Divisions to follow	July 2012



21 “In-Process” Counties

County Dashboard


County	Status	Target Date Provided
Nassau	Clericus Implementation Plan (FACC)	06/29/2012
Okaloosa	Working through Implementation Plan	06/01/2012
Osceola	Still working on migrating to new CMS with a planned completion for Civil cases by June	N/A
Pinellas	Working through Implementation Plan; 1 Division currently scheduled to be ready by target date, with the remaining divisions by 3 rd / 4 th Qtr. 2013	2013
Seminole	1 Division currently scheduled to be ready by target date, with the remaining divisions to follow	N/A



21 "In-Process" Counties

County Dashboard


County	Status	Target Date Provided
St. Johns	Working through Implementation Plan	N/A
Sumter	Clericus Implementation Plan (FACC)	06/01/2012
Taylor	Working through Implementation Plan	06/01/2012
Volusia	FACC will be providing infrastructure assistance requested by the county to augment their Implementation Plan	TBD



21 “In-Process” Counties

Near Term Work (February)

1. Establish Bi-Weekly Status Call
2. Request firm dates for Portal Capability for each county by division and by case type
3. Assess status, identify & prioritize issues, and determine where the FACC may help
4. Begin Project Manager local site visits, as requested, and where needed



21 "In-Process" Counties

Future Work (March/April)

1. Report Dashboard Status to the Florida Courts E-Filing Authority Board monthly
2. Develop a consolidated Master Implementation Schedule and Portal Readiness Matrix that addresses the status of **both the 21 "In-Process" counties and the 46 "Existing" counties**

Ongoing Work

1. Act as a liaison between county and FACC staff to achieve 100% compliance by target date
